

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2022							Sep 25, '22							Oct 2, '22							Oct 9, '22							Oct 16, '22							Oct 23, '22						
								T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S		
1		<b>Bend Work</b>	<b>21.25 days</b>	<b>Mon 9/26/22</b>	<b>Tue 10/25/22</b>																																												
2		Grade Prep Cooley & Stacy	0.5 days	Mon 9/26/22	Mon 9/26/22																																												
3		Grade Prep Cooley & 18th	1 day	Mon 9/26/22	Tue 9/27/22	2																																											
4		Grade Prep 18th and Egypt	1 day	Tue 9/27/22	Wed 9/28/22	3																																											
5		Place Concrete 3 Locations	1 day	Wed 9/28/22	Thu 9/29/22	4																																											
6		Backfill Locations	1 day	Thu 9/29/22	Fri 9/30/22	5																																											
7		Grade Prep 18th & Rorick	0.5 days	Wed 9/28/22	Wed 9/28/22	4																																											
8		Grade Prep 18th and Morningstar	1 day	Thu 9/29/22	Thu 9/29/22	7																																											
9		Grade Prep 18th & Sierra	0.5 days	Fri 9/30/22	Fri 9/30/22	8																																											
10		Grade Prep Purcell @ Pondo.	0.5 days	Fri 9/30/22	Fri 9/30/22	9																																											
11		Place Concrete 4 Locations	1 day	Mon 10/3/22	Mon 10/3/22	10																																											
12		Backfill Locations	1 day	Tue 10/4/22	Tue 10/4/22	11																																											
13		Grade Prep Yeoman @ Pine	1 day	Mon 10/3/22	Mon 10/3/22	10																																											
14		Grade Prep Deschutes Mkt @ Forest Service	0.25 days	Tue 10/4/22	Tue 10/4/22	13																																											
15		Grade Prep Deschutes Mkt & Butler Mkt	1 day	Tue 10/4/22	Wed 10/5/22	14																																											
16		Grade Prep Butler Mkt & Nasu Park	0.5 days	Wed 10/5/22	Wed 10/5/22	15																																											
17		Place Concrete 4 Locations	1 day	Wed 10/5/22	Thu 10/6/22	16																																											
18		Backfill Locations	1 day	Thu 10/6/22	Fri 10/7/22	17																																											


Project: Baseline Project Date: Wed 9/21/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2022							Sep 25, '22							Oct 2, '22							Oct 9, '22							Oct 16, '22							Oct 23, '22										
								T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S						
19		Grade Prep Butler Mkt & Weeping Willow	0.5 days	Wed 10/5/22	Thu 10/6/22	16																																															
20		Grade Prep Butler Mkt & Purcell	0.25 days	Thu 10/6/22	Thu 10/6/22	19																																															
21		Grade Prep Butler Mkt & Canal Park	1 day	Thu 10/6/22	Fri 10/7/22	20																																															
22		Place Concrete 3 Locations	1 day	Fri 10/7/22	Mon 10/10/22	21																																															
23		Backfill Locations	1 day	Mon 10/10/22	Tue 10/11/22	22																																															
24		Grade Prep Empire & Boyd Acres	1 day	Thu 10/6/22	Fri 10/7/22	20																																															
25		Grade Prep Boyd Acres & Brinson	0.5 days	Fri 10/7/22	Fri 10/7/22	24																																															
26		Grade Prep Boyd Acres & Ross	1 day	Mon 10/10/22	Mon 10/10/22	25																																															
27		Place Concrete 3 Locations	1 day	Tue 10/11/22	Tue 10/11/22	26																																															
28		Backfill Locations	1 day	Wed 10/12/22	Wed 10/12/22	27																																															
29		Grade Prep 9th @ Bend HS	1 day	Tue 10/11/22	Tue 10/11/22	26																																															
30		Grade Prep 9th & Woodland	0.5 days	Wed 10/12/22	Wed 10/12/22	29																																															
31		Grade Prep Wilson & Manley	0.25 days	Wed 10/12/22	Wed 10/12/22	30																																															
32		Place Concrete 3 Locations	1 day	Wed 10/12/22	Thu 10/13/22	31																																															
33		Backfill Locations	1 day	Thu 10/13/22	Fri 10/14/22	32																																															
34		Grade Prep 15th & Hollis	0.5 days	Wed 10/12/22	Thu 10/13/22	31																																															
35		Grade Prep 15th & Friar Tuck	1 day	Thu 10/13/22	Fri 10/14/22	34																																															
36		Grade Prep 15th & Sherwood	0.5 days	Fri 10/14/22	Fri 10/14/22	35																																															

Project: Baseline Project  
Date: Wed 9/21/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2022	Sep 25, '22	Oct 2, '22	Oct 9, '22	Oct 16, '22	Oct 23, '22																			
								T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
37		Grade Prep 15th & Murphy	0.25 days	Fri 10/14/22	Fri 10/14/22	36																										
38		Grade Prep Murphy & Brosterhous	0.25 days	Mon 10/17/22	Mon 10/17/22	37																										
39		Grade Prep Murphy & Countryside	1 day	Mon 10/17/22	Tue 10/18/22	38																										
40		Place Concrete 6 Locations	1 day	Tue 10/18/22	Wed 10/19/22	39																										
41		Backfill Locations	1 day	Wed 10/19/22	Thu 10/20/22	40																										
42		Grade Prep Powers & Parrell	1 day	Tue 10/18/22	Wed 10/19/22	39																										
43		Grade Prep Parrell & Badger	1 day	Wed 10/19/22	Thu 10/20/22	42																										
44		Grade Prep Murphy & Parrell	0.5 days	Thu 10/20/22	Thu 10/20/22	43																										
45		Grade Prep Murphy & Mel	0.5 days	Thu 10/20/22	Fri 10/21/22	44																										
46		Place Concrete 4 Locations	1 day	Fri 10/21/22	Mon 10/24/22	45																										
47		Backfill Locations	1 day	Mon 10/24/22	Tue 10/25/22	46																										
48		<b>Redmond Work</b>	<b>6 days</b>	<b>Mon 10/10/22</b>	<b>Mon 10/17/22</b>																											
49		St. Charkes Hospital Grade Prep	1 day	Mon 10/10/22	Mon 10/10/22																											
50		7th & Evergreen Grade Prep	1 day	Tue 10/11/22	Tue 10/11/22	49																										
51		Canal Blvd. Grade Prep	1 day	Wed 10/12/22	Wed 10/12/22	50																										
52		6th & Airport Grade Prep	1 day	Thu 10/13/22	Thu 10/13/22	51																										
53		Place Concrete Redmond Locations	1 day	Fri 10/14/22	Fri 10/14/22	52																										
54		Backfill Locations	1 day	Mon 10/17/22	Mon 10/17/22	53																										

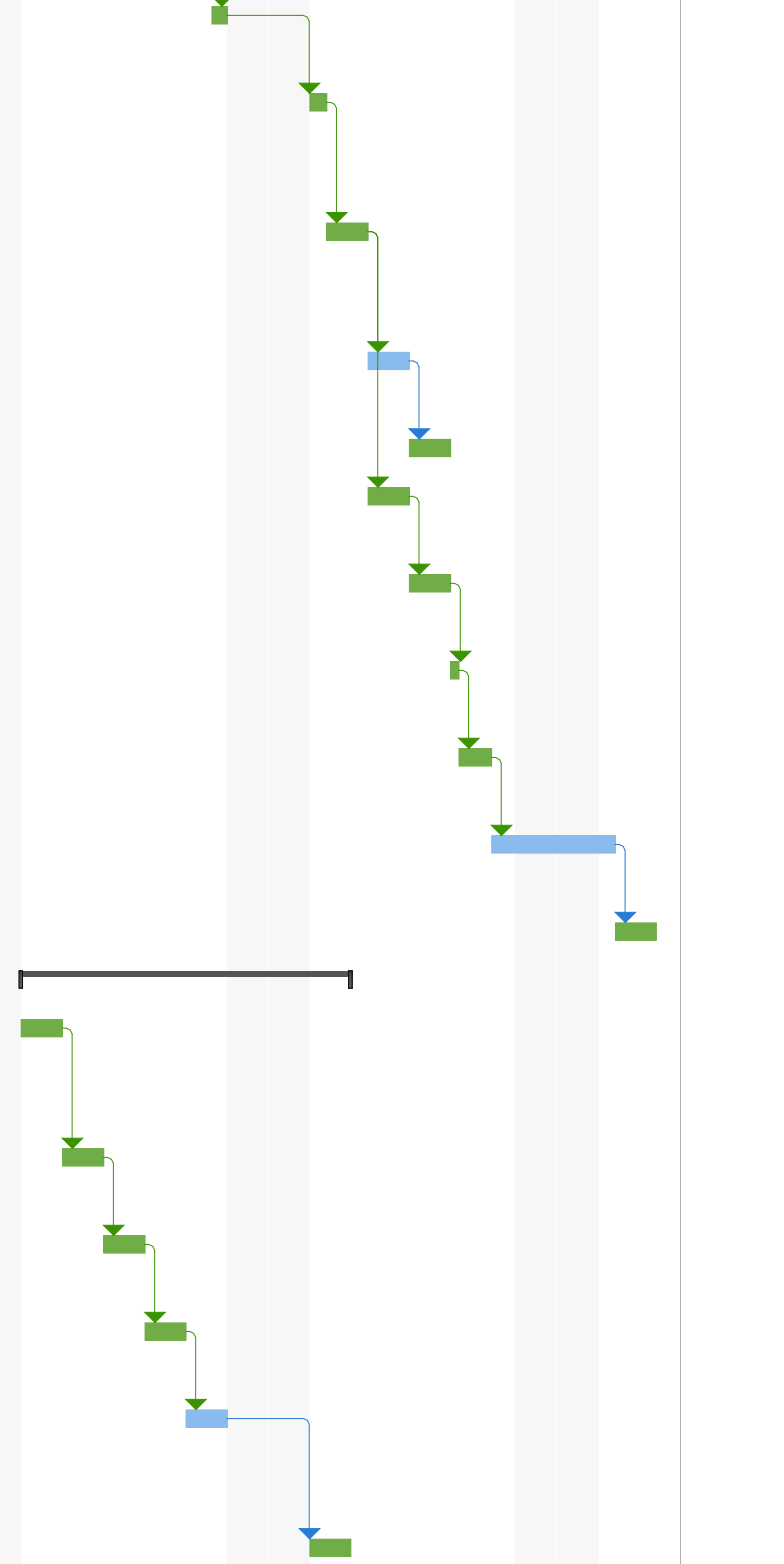

Project: Baseline Project Date: Wed 9/21/22	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			
